

**VIA ELECTRONIC SUBMISSION**

August 1, 2023

Canada Energy Regulator  
Suite 210, 517 Tenth Avenue S.W.  
Calgary, Alberta T2R 0A8

To: Ramona Sladic, Secretary of the Commission

Dear Ms. Sladic:

**Re: Trans Mountain Pipeline ULC (Trans Mountain)  
Trans Mountain Expansion Project (TMEP or Project)  
Condition 62: Construction Schedule  
File: OF-Fac-Oil-T260-2013-03 61**

Please find enclosed Trans Mountain's compliance filing in relation to Condition 62 pertaining to the following legal instruments, as amended:

- OC-065, (CPCN)
- AO-006-OC-2 (OC-2)
- AO-004-OC-49 (OC-49)
- AO-001-XO-T260-007-2016 (Temp)
- AO-002-XO-T260-008-2016 (Pump 1)
- AO-002-XO-T260-009-2016 (Pump 2)
- AO-002-XO-T260-010-2016 (Tanks)
- AO-001-MO-015-2016 (Deactivation)

The appended filing relates to all 39 phases identified in Trans Mountain's January 16, 2017 Phased Condition Matrix [[A81323-1](#)].

**Planned Activities**

The attached schedule summarizes Trans Mountain's forecast of planned activities based on current execution plans for the upcoming six-month period. Some of the activities forecast in the schedule are subject to regulatory approval and potential schedule changes. It should not be assumed the start dates for these activities will hold in the absence of the requisite approvals or changes to execution plans. Planned start dates and forecast end dates are subject to change where execution plans are revised or additional efficiencies in construction execution are determined. Additional activities may be added, or removed, as regulatory and permitting processes move forward and schedules for construction execution are updated.

Should you have any questions or wish to discuss this matter further, please contact the undersigned at [regulatory@transmountain.com](mailto:regulatory@transmountain.com) or (403) 514-6400.

Yours truly,

*Original signed by*

Tisha Homer  
Director, Regulatory  
Trans Mountain Canada Inc.

Enclosure:  
TMEP Construction Summary Schedule (6-Month Look Ahead)

**Attachment 1**

**Condition 62**

**All Phases**

**Construction Schedule 6 Month Look Ahead**



# TMEP Construction Summary Schedule (6-month Look Ahead )

Cut off Date: 31-Jul-23

Major Project Activities	2023						2024
	July	August	September	October	November	December	January
<b>Pipelines</b>							
<b>Spread 2 (KP 49-338)</b>							
Machine & Final Clean Up	Actual	Forecast					
<b>Spread 3 &amp; 4A (KP 489-690)</b>							
String, Weld, Tie-ins (KP 489 - 565)	Actual						
String, Weld, Tie-ins (KP 565 - 610)	Actual						
String, Weld, Tie-ins (KP 610 - 690)	Actual						
Stove Pipe & Steep Slope	Actual						
Hydrostatic Testing & Valve Installation	Actual	Forecast					
Machine & Final Clean Up	Actual	Forecast					
<b>Spread 4B (KP 690-765)</b>							
Machine & Final Clean Up	Actual	Forecast					
<b>Spread 5A (KP 806-987)</b>							
Mainline Strip, Grade & Blast	Actual						
Mainline String, Weld, Tie-ins (KP 928-987)	Actual	Forecast					
Major Trenchless Crossings	Actual	Forecast					
Jacko Lake Microtunnel & Pipe Installation (KP 852-856)	Actual	Forecast					
Hydrostatic Testing & Final Tie-ins	Actual	Forecast					
Valve Installation	Actual	Forecast					
Machine & Final Clean Up (Seeding)	Actual	Forecast					
<b>Spread 5B (KP 987-1075)</b>							
Mainline Access	Actual						
ROW Preparation	Actual	Forecast					
Strip, Grade & Blast	Actual	Forecast					
Mainline String, Weld & Tie-ins (KP 987-1016)	Actual	Forecast					
Technical Challenge Areas (KP 1012-1016)	Actual	Forecast					
String, Weld & Tie-ins Mainline & TCA's KB (KP 1016-1038.1)	Actual	Forecast					
String, Weld & Tie-ins Mainline & TCA's Macro (KP 1038.1-1075)	Actual	Forecast					
Major Trenchless Crossings	Actual	Forecast					
Hydrostatic Testing & Valve Installation	Actual	Forecast					
Machine & Final Clean Up	Actual	Forecast					
<b>Spread 6 (KP 1075-1145)</b>							
Access & Grade	Actual						
Fraser Valley & Chilliwack - String, Weld & Tie-ins (KP 1075 - 1100)	Actual	Forecast					
Abbotsford - String, Weld & Tie-ins (KP 1100 - 1128)	Actual	Forecast					
Langley - String, Weld & Tie-ins (KP 1128-1145)	Actual	Forecast					
HDB & GHAB Crossings & Trench Box	Actual	Forecast					


Notes: The schedule may be subject to change due to regulatory, permits, lands & 3rd party crossing agreements.

Legend: ■ Actual ■ Forecast



# TMEP Construction Summary Schedule (6-month Look Ahead )

Cut off Date: 31-Jul-23

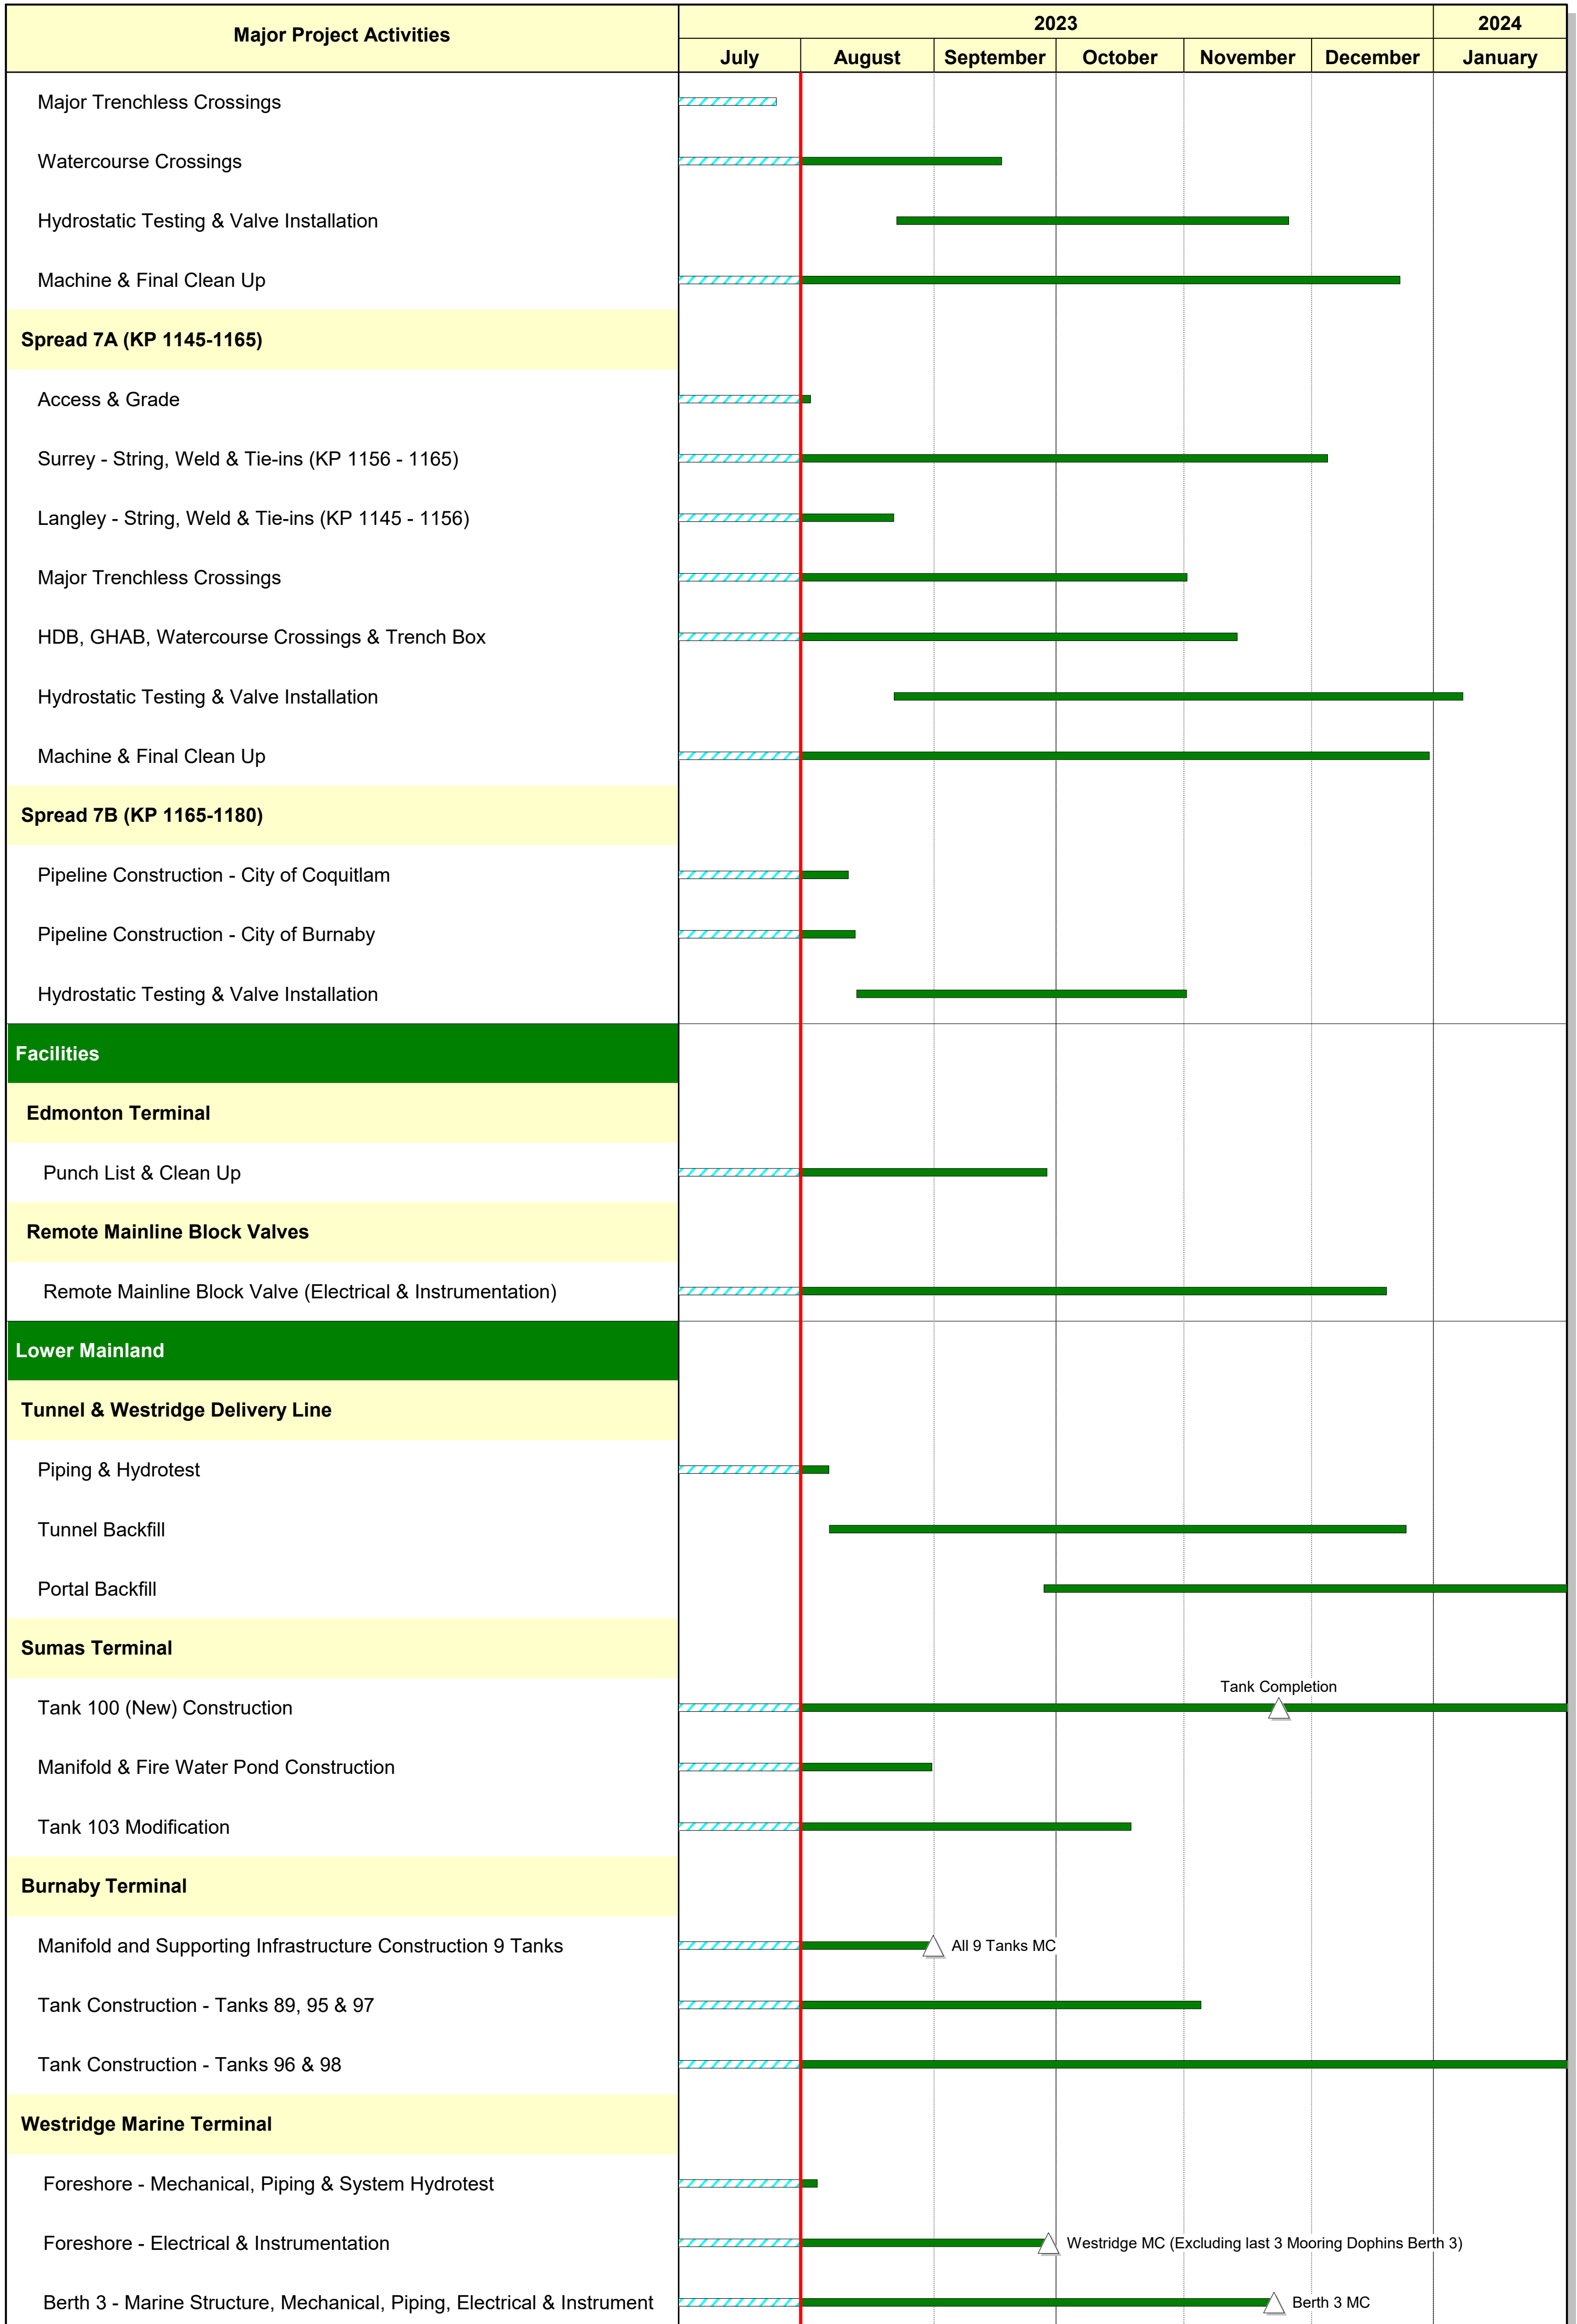

Notes: The schedule may be subject to change due to regulatory, permits, lands & 3rd party crossing agreements.

Legend: █ Actual █ Forecast
